

# Half-Cent Sales Surtax Citizen Advisory Committee (CAC)

Annual Report – January 2018



# Half-Cent Sales Surtax CAC

## Annual Report – January 2018

- Resolution 2015-30:
  - The School Board asked St. Johns County voters to approve a Half-Cent Sales Surtax for critical capital infrastructure
  - Called for the formation of a Citizen Advisory Committee (CAC) to advise and monitor the expenditure of the sales tax proceeds
  - Requires an annual report of the CAC in January
- On November 3<sup>rd</sup>, 2015, the voters approved the Half-Cent Sales Surtax
- Collections began on January 1, 2016

# Half-Cent Sales Surtax CAC

## Annual Report – January 2018

- Selection of the Citizen Advisory Committee
  - Call for Applications
  - Each School Board Member selected 3 citizen members and an alternate from their District on February 9, 2016
  - Collectively the Committee has varied and relevant experience to the four areas of expenditure
- Committee selected a Chairman, Vice Chairman and Secretary
- Meetings are held quarterly
- School Board will consider reappointments and fill vacancies in February 2018

# Half-Cent Sales Surtax CAC

## Annual Report – January 2018

**Chairman: Mr. Bill McCormick**  
**Vice Chairman: TBD**  
**Secretary: TBD**

<b>District 1</b>	<b>Term</b>
Melissa Nelson	3 Years
Shannon McCormick	2 Years
John Quattrochi	2 Years
Alternate: Norvie Veracruz	

<b>District 2</b>	<b>Term</b>
Thomas Cave	3 Years
Victor Raymos	2 Years
Barbara Little	2 Years
Alternate: <i>TBD</i>	

<b>District 3</b>	<b>Term</b>
Edward Albanesi	3 Years
<i>TBD</i>	2 Years
Frederick Danner	2 Years
Alternate: <i>TBD</i>	

<b>District 4</b>	<b>Term</b>
Steven Olsen	3 Years
John Hardman	2 Years
Hugh Rappa	2 Years
Alternate: Damian Cook	

<b>District 5</b>	<b>Term</b>
Susan Connor	3 Years
Bill McCormick	2 Years
Mark Simpson	2 Years
Alternate: Grant Misterly	

# Half-Cent Sales Surtax CAC

## Annual Report – January 2018

- Half-Cent Sales Surtax allows Capital Expenditure for
  - New Construction
  - Reconstruction
  - Improvement of School Facilities
    - Safety & Security Improvements
    - Technology Upgrades

# Half-Cent Sales Surtax CAC

## Annual Report – January 2018

### Critically Needed Project List

<b>Meet the Needs of an Increasing Student Population</b>	<b>\$106,000,000</b>
<b>Maintain High Quality Educational Facilities</b>	<b>\$ 14,000,000</b>
<b>Provide New Technology to Prepare Children for 21st Century Learning</b>	<b>\$ 25,000,000</b>
<b>Continue to Keep our Children Safe</b>	<b>\$ 5,000,000</b>

---

**\$150,000,000**

# Half-Cent Sales Surtax CAC

## Annual Report – January 2018

- Half-Cent Sales Surtax projected revenue
  - \$150,000,000 over 10 years
  - \$13,000,000 per year
- In February 2016, SJCSD bonded \$50,000,000 with an interest rate of 1.72% for construction of
  - Picolata Crossing Elementary (M): **Pacetti Road**
  - K-8 School LL: **Aberdeen**





# Half-Cent Sales Surtax: Annual Report – January 2018

Progress: 2016-2017 Budget





# Half-Cent Sales Surtax: Annual Report – January 2018

## Progress: 2016-2017 Budget

Meet the Needs of an Increasing Student Population	\$106,000,000
--	---------------

- |   |                     |
|---|---------------------|
| • <u>K-8 School LL</u> : Northwest K-8 school – Greenbriar Rd /<br>Longleaf Pine Pkwy area – Aberdeen | \$ 36,575,480       |
| • <u>Elementary M</u> : Central elementary – World Golf Village area                                  | \$ 23,800,000       |
| • <u>K-8 School KK</u> : Nocatee  | \$ <u>5,583,207</u> |

Total Budgeted	\$ 65,958,687
----------------	---------------

Total Remaining	\$ 40,041,313
-----------------	---------------

# Half-Cent Sales Surtax CAC Annual Report – January 2018



## Picolata Crossing Elementary School M

2675 Pacetti Road, St. Augustine, FL 32092

Opened 2017-2018 SY

Student Capacity: 871 students

Budget: \$23,800,000



# Half-Cent Sales Surtax CAC Annual Report – January 2018



## New K-8 School LL

1365 Shetland Drive, St. Johns, FL 32259

Opening 2018-2019 SY

Student Capacity: 1,490 students

Budget: \$36,575,480

# Half-Cent Sales Surtax CAC Annual Report – January 2018



## New K-8 School LL

1365 Shetland Drive, St. Johns, FL 32259

Opening 2018-2019 SY

Student Capacity: 1,490 students

Budget: \$36,575,480



# Half-Cent Sales Surtax CAC Annual Report – January 2018



## New K-8 School KK

2135 Palm Valley Road, Ponte Vedra, FL 32081

Opening 2018-2019 SY

Student Capacity: 1,490 students

Budget: \$5,583,207



# Half-Cent Sales Surtax CAC Annual Report – January 2018



## New K-8 School KK

2135 Palm Valley Road, Ponte Vedra, FL 32081

Opening 2018-2019 SY

Student Capacity: 1,490 students

Budget: \$5,583,207



# Half-Cent Sales Surtax: Annual Report – January 2018

## Progress: 2016-2017 Budget

<b>Maintain High Quality Educational Facilities</b>	<b>\$14,000,000</b>
---	---------------------

Roof replacements – <u>Hartley</u> , Ketterlinus	\$ 670,500
--	------------



Total Budgeted	\$ 670,500
----------------	------------

Total Remaining	\$13,329,500
-----------------	--------------



Roof  
replacement  
– Hartley  
Elementary:

BEFORE


**Hartley Elementary School**



# Roof replacement – Hartley Elementary:

## BEFORE

### Hartley Elementary School

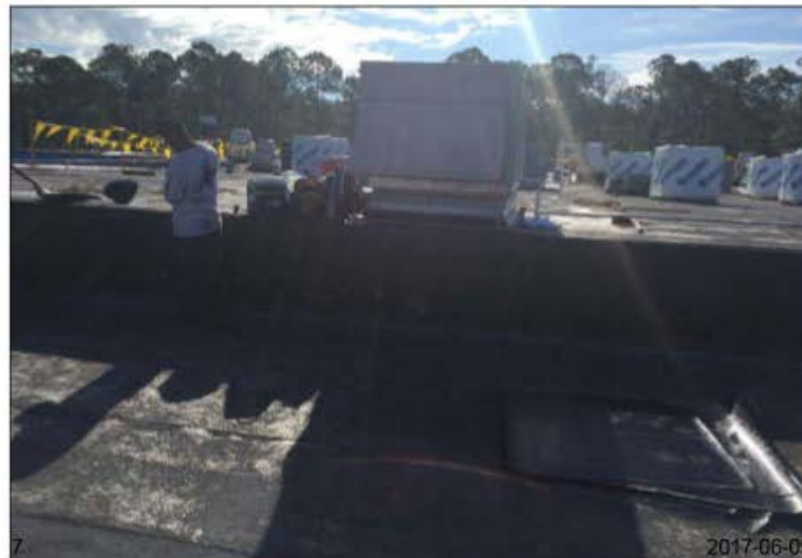



# Roof replacement – Hartley Elementary:

## AFTER

### SJCSD/Hartley Elementary School



## SJCSD/Hartley Elementary School

Roof  
replacement  
– Hartley  
Elementary:

AFTER





# Half-Cent Sales Surtax: Annual Report – January 2018

## Progress: 2016-2017 Budget

<b>Maintain High Quality Educational Facilities</b>	<b>\$14,000,000</b>
---	---------------------

<b>Roof replacements – Hartley, <u>Ketterlinus</u></b>	<b>\$ 670,500</b>
--	-------------------



Total Budgeted	\$ 670,500
----------------	------------

Total Remaining	\$13,329,500
-----------------	--------------

Roof  
replacement  
– Ketterlinus  
Elementary:

BEFORE

**SJCSD/Ketterlinus Elementary School**





## SJCSD/Ketterlinus Elementary School

Roof  
replacement  
– Ketterlinus  
Elementary:

AFTER



5

2017-08-21



6

2017-08-21



7

2017-08-21



8

2017-08-21



Roof  
replacement  
– Ketterlinus  
Elementary:

AFTER

## SJCSD/Ketterlinus Elementary School



1

2017-08-21



2

2017-08-21



3

2017-08-21



4

2017-08-21

# Half-Cent Sales Surtax: Annual Report – January 2018

## Progress: 2016-2017 Budget

<b>Continue to Keep our Children Safe</b>	<b>\$5,000,000</b>
---	--------------------

- |   |            |
|---|------------|
| <ul style="list-style-type: none"><li>• 800 MHz radios for school buses</li></ul> | \$ 858,366 |
|---|------------|

Total Budgeted	\$ 858,366
----------------	------------

Total Remaining	\$4,141,634
-----------------	-------------

# Half-Cent Sales Surtax CAC Annual Report – January 2018




## Motorola Radio Enhancement System for School Buses

Budget: \$921,392

Actual: \$858,366

### Benefits:

- Direct Communication with Emergency Responders & Buses
- Essential Communication link during Hurricanes Matthew and Irma

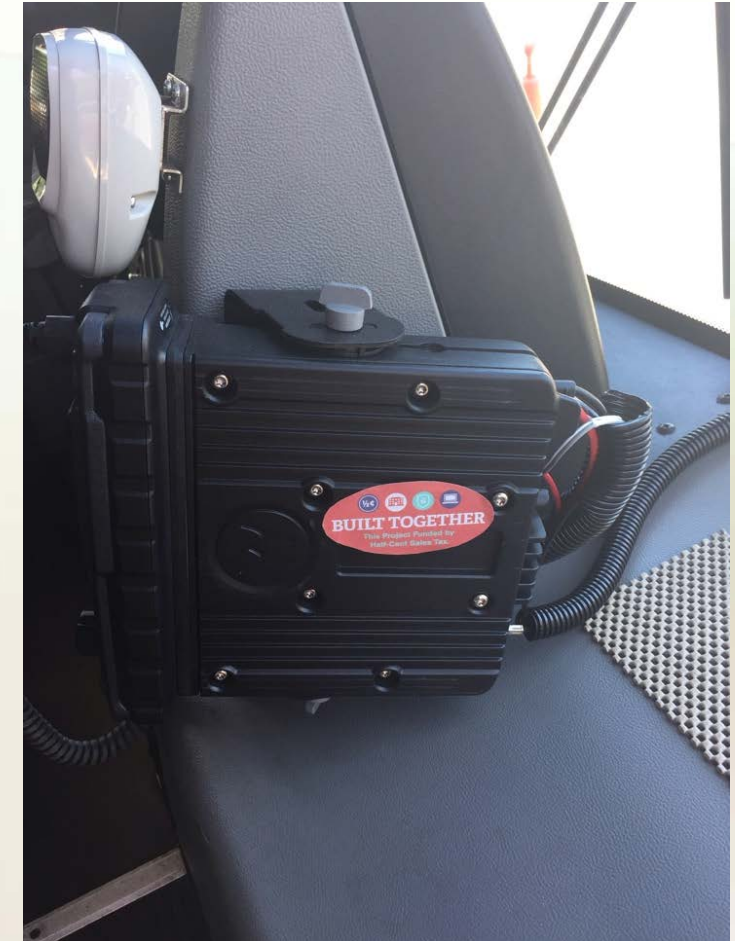

# Half-Cent Sales Surtax CAC Annual Report – January 2018:

## Financial Report

St. Johns County School Board  
Half-Cent Sales Tax Citizens Advisory Committee  
Financial Report - As of November 30, 2017

	Budget	Actual	Encumbrance	Balance
<b>SALES TAX FUNDS: (Bond Proceeds &amp; Sales Tax Revenue)</b>				
<b>PICOLATA CROSSING ELEMENTARY - "M"</b>				
<b>(World Golf Village Area)</b>				
Construction	\$ 22,131,001.12	\$19,985,943.60	\$ 561,279.47	\$ 1,583,778.05
Start-Up Equipment	\$ 1,613,190.00	\$ 1,384,816.40	\$ 23,304.20	\$ 205,069.40
Other Related Costs	\$ 55,808.88	\$ 52,818.88	\$ 2,990.00	\$ 0.00
<b>TOTAL PICOLATA CROSSING ELEMENTARY</b>	<b>\$ 23,800,000.00</b>	<b>\$21,423,578.88</b>	<b>\$ 587,573.67</b>	<b>\$ 1,788,847.45</b>
<b>NEW K-8 SCHOOL "LL":</b>				
<b>(Aberdeen Area)</b>				
Construction	\$ 36,558,158.68	\$13,064,269.79	\$ 22,452,544.35	\$ 1,041,344.54
Start-Up Equipment	\$ 2,500,000.00	\$ -	\$ -	\$ 2,500,000.00
Other Related Costs	\$ 17,321.20	\$ 16,511.20	\$ 810.00	\$ -
<b>TOTAL NEW K-8 SCHOOL "LL"</b>	<b>\$ 39,075,479.88</b>	<b>\$13,080,780.99</b>	<b>\$ 22,453,354.35</b>	<b>\$ 3,541,344.54</b>
<b>NEW K-8 SCHOOL "KK":</b>				
<b>(Nocatee Area)</b>				
Construction	\$ 5,583,206.63	\$ -	\$ 4,743,076.66	\$ 840,129.97
<b>TOTAL NEW K-8 "KK" (SALES TAX FUNDS)</b>	<b>\$ 5,583,206.63</b>	<b>\$ -</b>	<b>\$ 4,743,076.66</b>	<b>\$ 840,129.97</b>
<b>MOTOROLA RADIO ENHANCEMENT SYSTEM</b>				
FOR SCHOOL BUSES	\$ 858,365.58	\$ 858,365.58	\$ -	\$ -
<b>HARTLEY ELEMENTARY ROOFING PROJECT</b>				
	\$ 479,000.00	\$ 301,216.93	\$ 177,783.07	\$ -
<b>KETTERLINUS ELEMENTARY ROOFING PROJECT</b>				
	\$ 191,500.00	\$ 150,290.73	\$ 41,209.27	\$ -
<b>TOTAL ALL SALES TAX FUNDS</b>	<b>\$ 69,987,552.09</b>	<b>\$35,814,233.11</b>	<b>\$ 28,002,997.02</b>	<b>\$ 6,170,321.96</b>
<b>OTHER FUNDS: (Impact Fees, Proportionate Share &amp; 1.5 Mills)</b>				
<b>NEW K-8 SCHOOL "KK":</b>				
Construction	\$ 37,075,937.58	\$16,356,158.53	\$ 16,219,774.48	\$ 4,500,004.57
Other Related Costs	\$ 50,308.79	\$ 45,073.29	\$ 5,235.50	\$ -
<b>TOTAL NEW K-8 SCHOOL "KK" (OTHER)</b>	<b>\$ 37,126,246.37</b>	<b>\$16,401,231.82</b>	<b>\$ 16,225,009.98</b>	<b>\$ 4,500,004.57</b>
<b>TOTAL NEW K-8 SCHOOL "KK" (ALL FUNDS)</b>	<b>\$ 42,709,453.00</b>	<b>\$16,401,231.82</b>	<b>\$ 20,968,086.64</b>	<b>\$ 5,340,134.54</b>

**St. Johns County School Board  
Half-Cent Sales Tax Citizens Advisory Committee  
Financial Report - As of November 30, 2017**

**Half-Cent  
Sales  
Surtax  
CAC  
Annual  
Report –  
January  
2018:**

**Financial  
Report**

	Budget	Actual	Encumbrance	Balance
<b>SALES TAX FUNDS: (Bond Proceeds &amp; Sales Tax Revenue)</b>				
<b>PICOLATA CROSSING ELEMENTARY - "M"</b>				
<b>(World Golf Village Area)</b>				
Construction	\$ 22,131,001.12	\$19,985,943.60	\$ 561,279.47	\$ 1,583,778.05
Start-Up Equipment	\$ 1,613,190.00	\$ 1,384,816.40	\$ 23,304.20	\$ 205,069.40
Other Related Costs	\$ 55,808.88	\$ 52,818.88	\$ 2,990.00	\$ 0.00
<b>TOTAL PICOLATA CROSSING ELEMENTARY</b>	<b>\$ 23,800,000.00</b>	<b>\$21,423,578.88</b>	<b>\$ 587,573.67</b>	<b>\$ 1,788,847.45</b>
<b>NEW K-8 SCHOOL "LL":</b>				
<b>(Aberdeen Area)</b>				
Construction	\$ 36,558,158.68	\$13,064,269.79	\$ 22,452,544.35	\$ 1,041,344.54
Start-Up Equipment	\$ 2,500,000.00	\$ -	\$ -	\$ 2,500,000.00
Other Related Costs	\$ 17,321.20	\$ 16,511.20	\$ 810.00	\$ -
<b>TOTAL NEW K-8 SCHOOL "LL"</b>	<b>\$ 39,075,479.88</b>	<b>\$13,080,780.99</b>	<b>\$ 22,453,354.35</b>	<b>\$ 3,541,344.54</b>
<b>NEW K-8 SCHOOL "KK":</b>				
<b>(Nocatee Area)</b>				
Construction	\$ 5,583,206.63	\$ -	\$ 4,743,076.66	\$ 840,129.97
<b>TOTAL NEW K-8 "KK" (SALES TAX FUNDS)</b>	<b>\$ 5,583,206.63</b>	<b>\$ -</b>	<b>\$ 4,743,076.66</b>	<b>\$ 840,129.97</b>



**St. Johns County School Board  
Half-Cent Sales Tax Citizens Advisory Committee  
Financial Report - As of November 30, 2017**

Half-Cent  
Sales  
Surtax  
CAC  
Annual  
Report –  
January  
2018:

Financial  
Report

	Budget	Actual	Encumbrance	Balance
<b>MOTOROLA RADIO ENHANCEMENT SYSTEM FOR SCHOOL BUSES</b>	\$ 858,365.58	\$ 858,365.58	\$ -	\$ -
<b>HARTLEY ELEMENTARY ROOFING PROJECT</b>	\$ 479,000.00	\$ 301,216.93	\$ 177,783.07	\$ -
<b>KETTERLINUS ELEMENTARY ROOFING PROJECT</b>	\$ 191,500.00	\$ 150,290.73	\$ 41,209.27	\$ -
<b>TOTAL ALL SALES TAX FUNDS</b>	<u>\$ 69,987,552.09</u>	<u>\$35,814,233.11</u>	<u>\$ 28,002,997.02</u>	<u>\$ 6,170,321.96</u>
<b>OTHER FUNDS: (Impact Fees, Proportionate Share &amp; 1.5 Mills)</b>				
<b>NEW K-8 SCHOOL "KK":</b>				
Construction	\$ 37,075,937.58	\$16,356,158.53	\$ 16,219,774.48	\$ 4,500,004.57
Other Related Costs	\$ 50,308.79	\$ 45,073.29	\$ 5,235.50	\$ -
<b>TOTAL NEW K-8 SCHOOL "KK" (OTHER)</b>	<b>\$ 37,126,246.37</b>	<b>\$16,401,231.82</b>	<b>\$ 16,225,009.98</b>	<b>\$ 4,500,004.57</b>
<b>TOTAL NEW K-8 SCHOOL "KK" (ALL FUNDS)</b>	<u><b>\$ 42,709,453.00</b></u>	<u><b>\$16,401,231.82</b></u>	<u><b>\$ 20,968,086.64</b></u>	<u><b>\$ 5,340,134.54</b></u>



# Half-Cent Sales Surtax Annual Report – January 2018

2017-2018 Budget





# Half-Cent Sales Surtax: Annual Report – January 2018

- Projected 2017-2018 Surtax Revenue  
\$18,624,805
- Debt Service \$5,639,350



# Half-Cent Sales Surtax: Annual Report – January 2018 2017-2018 Budget



<b>Meet the Needs of an Increasing Student Population</b>	<b>\$106,000,000</b>
New Construction	
• K-8 School LL: Furniture, Fixtures & Equipment	\$ 2,500,000
School Expansions	
• Switzerland Point Middle School Dining Expansion	\$ 750,000
• Patriot Oaks Academy Dining Expansion	\$ 750,000
• Savings for Future School Construction/Expansion	\$ <u>1,844,891</u>
Total	\$ 5,844,891

# Half-Cent Sales Surtax: Annual Report – January 2018 2017-2018 Budget



## Maintain High Quality Educational Facilities

**\$14,000,000**

### Roofs

- Mill Creek Elementary Phase 2 Roof Replacement \$ 200,000
- Marjorie K. Rawlings Elementary Phase 1 Roof Replacement \$ 850,000

### PE, Playground & Athletic Facility Improvements

- RB Hunt Covered PE Area & Restrooms \$ 250,000

### Site Improvements

- The Webster School Full Site Utilization:  
Bus Loop, Parking & Fencing Upgrades \$ 250,000
- Murray Middle School Site Improvements \$ 165,000

Total \$ 1,715,000

# Half-Cent Sales Surtax: Annual Report – January 2018 2017-2018 Budget



## **Provide New Technology to Prepare Children for 21st Century Learning** **\$25,000,000**

### Classroom Technology Tools

- Classroom Technology Upgrades: 34 Schools \$ 1,300,000

### Student & Teacher Instructional Devices

- Student & Teacher Instructional Devices: 36 schools \$ 2,016,000

### Infrastructure Improvements

- Wireless Access Points Upgrades: 8 Schools \$ 724,010
- Uninterrupted Power Supply Replacement: 9 Schools \$ 192,000
- Total \$ 4,232,010

# Half-Cent Sales Surtax: Annual Report – January 2018 2017-2018 Budget



## **Continue to Keep our Children Safe**

**\$5,000,000**

### Security Cameras & Monitoring Systems

- Security Cameras at 24 schools \$ 345,085
- Upgrade Alarm System at Fruit Cove Middle School \$ 2,500
- Upgrade Intercom Systems: 6 schools \$ 165,585

### Fencing

- Fencing at 9 schools \$ 84,519

### Security Doors & Entrances

- Single Point of Entry Improvements at 14 schools \$ 239,025
- School Security Improvements at 7 schools (approx) \$ 176,720
- Exterior Lighting at Sebastian Middle School \$ 10,000
  
- Zonar School Bus GPS Technology \$ 111,220

Total

**\$1,134,654**

# Half-Cent Sales Surtax CAC Annual Report – January 2018

## Funding Summary:

Collection Month	Date Received	Amount	Debt	Capital
July	9/27/2017	\$ 1,492,221.71	\$ 156,812.50	\$ 1,335,409.21
August	10/25/2017	\$ 1,287,261.21	\$ 153,312.50	\$ 1,133,948.71
September	11/27/2017	\$ 1,207,091.55	\$ 153,312.50	\$ 1,053,779.05
September Qtrly	11/9/2017	\$ 502,241.85	\$ -	\$ 502,241.85
October	Projected	\$ 1,335,705.26	\$ 153,312.50	\$ 1,182,392.76
November	Projected	\$ 1,362,205.96	\$ 153,312.50	\$ 1,208,893.46
December	Projected	\$ 1,671,101.31	\$ 153,312.50	\$ 1,517,788.81
December Qtrly	Projected	\$ 300,000.00	\$ -	\$ 300,000.00
January	Projected	\$ 1,226,959.40	\$ 795,812.50	\$ 431,146.90
February	Projected	\$ 1,316,424.46	\$ 795,812.50	\$ 520,611.96
March	Projected	\$ 1,633,785.81	\$ 795,812.50	\$ 837,973.31
March Qtrly	Projected	\$ 300,000.00	\$ -	\$ 523,803.20
April	Projected	\$ 1,468,128.20	\$ 795,812.50	\$ 672,315.70
May	Projected	\$ 1,677,498.28	\$ 795,812.50	\$ 881,685.78
June	Projected	\$ 1,490,910.39	\$ 795,812.50	\$ 695,097.89
June Qtrly	Projected	\$ 300,000.00	\$ -	\$ 300,000.00
<b>17/18 Actual</b>		\$ 4,488,816.32	\$ 310,125.00	\$ 10,547,989.22
<b>17/18 Projected</b>		\$ 14,082,719.08	\$ 5,388,125.00	\$ 2,549,099.38
<b>Total 17/18 Actual and Projected</b>		<u>\$ 18,571,535.40</u>	<u>\$ 5,698,250.00</u>	<u>\$ 13,097,088.60</u>

<b>17/18 Projected for Budget</b>	<u>\$ 18,624,805.00</u>
<b>Increase/(Decrease) over Projected Budget</b>	<u>\$ (53,269.60)</u>

\*Quarterly amounts reflect Out of County purchases, which are remitted on a quarterly basis

<b>Cumulative Interest Earned thru 11/30/17:</b>	
Fund 397 - Bond Proceeds	\$ 630,004.20
Fund 396 - Sales Tax Revenue	\$ 182,586.50
<b>Total Interest Earned</b>	<u>\$ 812,590.70</u>

Recap		averages
\$ 17,169,293.55	M	\$ 1,430,774.46
\$ 1,402,241.85	Q	\$ 350,560.46
\$ 18,571,535.40		



# Half-Cent Sales Surtax CAC Annual Report – January 2018

## Funding Summary:

Collection Month	Date Received	Amount		Debt		Capital
July	9/27/2017	\$ 1,492,221.71		\$ 156,812.50		\$ 1,335,409.21
August	10/25/2017	\$ 1,287,261.21		\$ 153,312.50		\$ 1,133,948.71
September	11/27/2017	\$ 1,207,091.55		\$ 153,312.50		\$ 1,053,779.05
September Qtrly	11/9/2017	\$ 502,241.85		\$ -		\$ 502,241.85
October	Projected	\$ 1,335,705.26		\$ 153,312.50		\$ 1,182,392.76
November	Projected	\$ 1,362,205.96		\$ 153,312.50		\$ 1,208,893.46
December	Projected	\$ 1,671,101.31		\$ 153,312.50		\$ 1,517,788.81
December Qtrly	Projected	\$ 300,000.00		\$ -		\$ 300,000.00
January	Projected	\$ 1,226,959.40		\$ 795,812.50		\$ 431,146.90
February	Projected	\$ 1,316,424.46		\$ 795,812.50		\$ 520,611.96
March	Projected	\$ 1,633,785.81		\$ 795,812.50		\$ 837,973.31
March Qtrly	Projected	\$ 300,000.00		\$ -		\$ 523,803.20
April	Projected	\$ 1,468,128.20		\$ 795,812.50		\$ 672,315.70
May	Projected	\$ 1,677,498.28		\$ 795,812.50		\$ 881,685.78
June	Projected	\$ 1,490,910.39		\$ 795,812.50		\$ 695,097.89
June Qtrly	Projected	\$ 300,000.00		\$ -		\$ 300,000.00
<b>17/18 Actual</b>		\$ 4,488,816.32		\$ 310,125.00		\$ 10,547,989.22
<b>17/18 Projected</b>		\$ 14,082,719.08		\$ 5,388,125.00		\$ 2,549,099.38
<b>Total 17/18 Actual and Projected</b>		<u>\$ 18,571,535.40</u>		<u>\$ 5,698,250.00</u>		<u>\$ 13,097,088.60</u>



# Half-Cent Sales Surtax CAC Annual Report – January 2018

## Funding Summary:

17/18 Projected for Budget	\$ 18,624,805.00
Increase/(Decrease) over Projected Budget	<u>\$ (53,269.60)</u>

\*Quarterly amounts reflect Out of County purchases, which are remitted on a quarterly basis

### Cumulative Interest Earned thru 11/30/17:

Fund 397 - Bond Proceeds	\$ 630,004.20
Fund 396 - Sales Tax Revenue	<u>\$ 182,586.50</u>
<b>Total Interest Earned</b>	<b><u>\$ 812,590.70</u></b>

Recap		averages
\$ 17,169,293.55	M	\$ 1,430,774.46
\$ 1,402,241.85	Q	\$ 350,560.46
\$ 18,571,535.40		

# Half-Cent Sales Surtax CAC Annual Report – January 2018



- Priorities for 2018-2019 Budget:
  - Safety & Security
  - Technology
  - School Expansions
  - Improvement of Facilities
  - Savings for New School Construction
